



October 30, 2019


RE: 247 Worth Avenue Buildout

We propose to install a green wall at the end of the hallway leading to the building at 247 Worth Avenue. We believe this should isolate the work from Worth Avenue proper. We would also like to offer the utilization of the Apollo Parking lot as the only access to the site. That way we will also not need or request a parking permit for Worth Avenue proper. We would like our working hours to be normal seasonal hours and overtime if you would allow. We will endeavor to make as many saw cuts inside the building as we can to mitigate the noise.

Our schedule would be as follows:

November 13th -15th : Town Approvals
November 18th – 22nd : Continue Demolition
November 25th – 29th : No Work
December 2nd – 20th : Continue Demolition
December 23rd – 27th : No Work
December 30th – January 3rd : No Work
January 6th – 31st : Framing & Start Rough MEP
February 3rd – 28th : MEP Rough, Windows & Screw Walls
March 2nd – 31st : Stucco Patching, Start Drywall, Tile & Pavers
April 1st – 30th : Painting & MEP Trim
May 1st – 29th : Finishes, Punch & Finals

Building upon a lifetime of experience

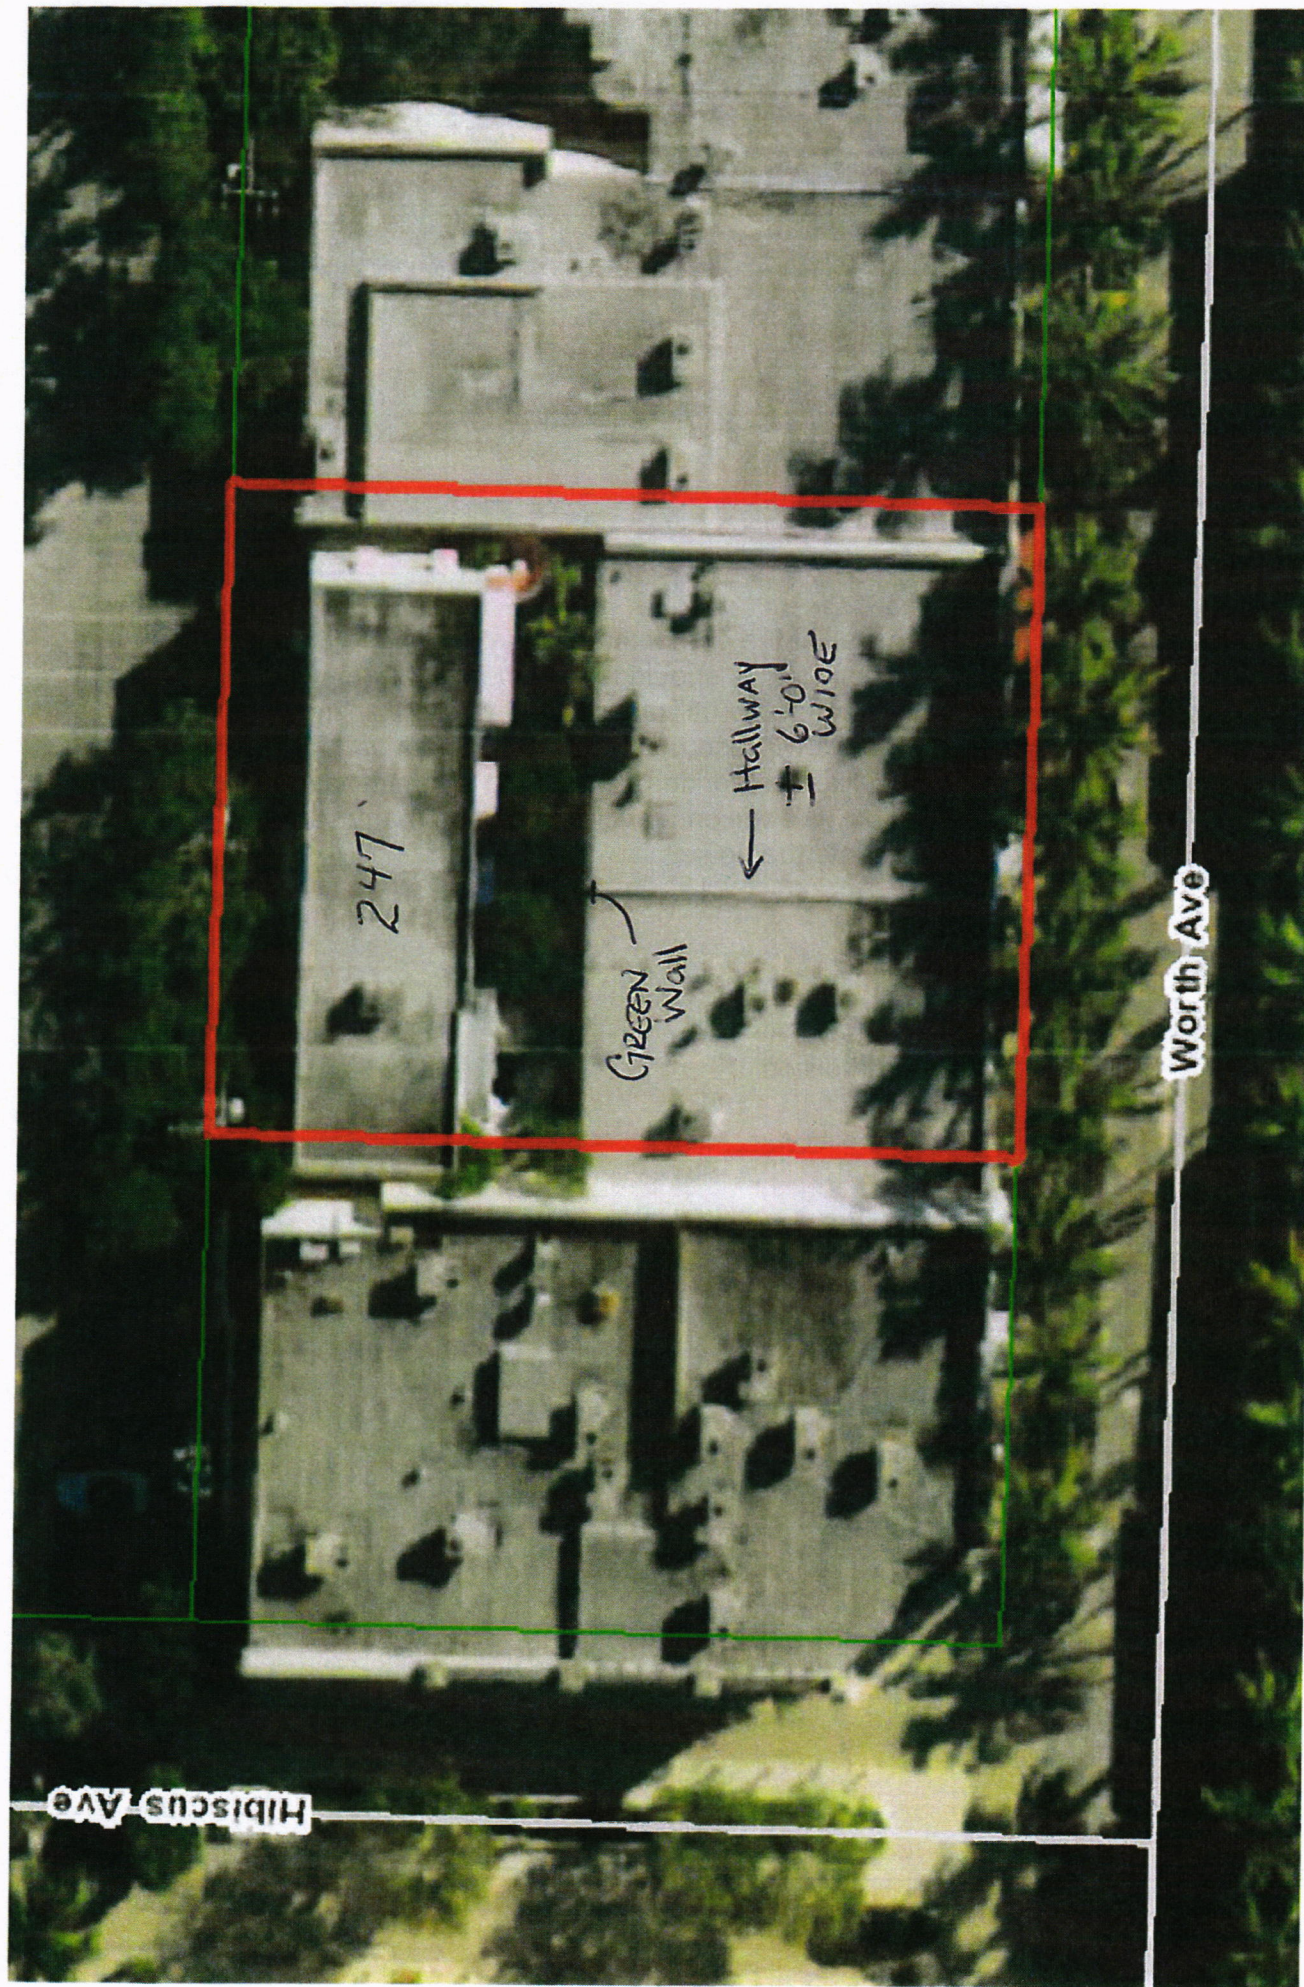

Hibiscus Ave

Worth Ave
