




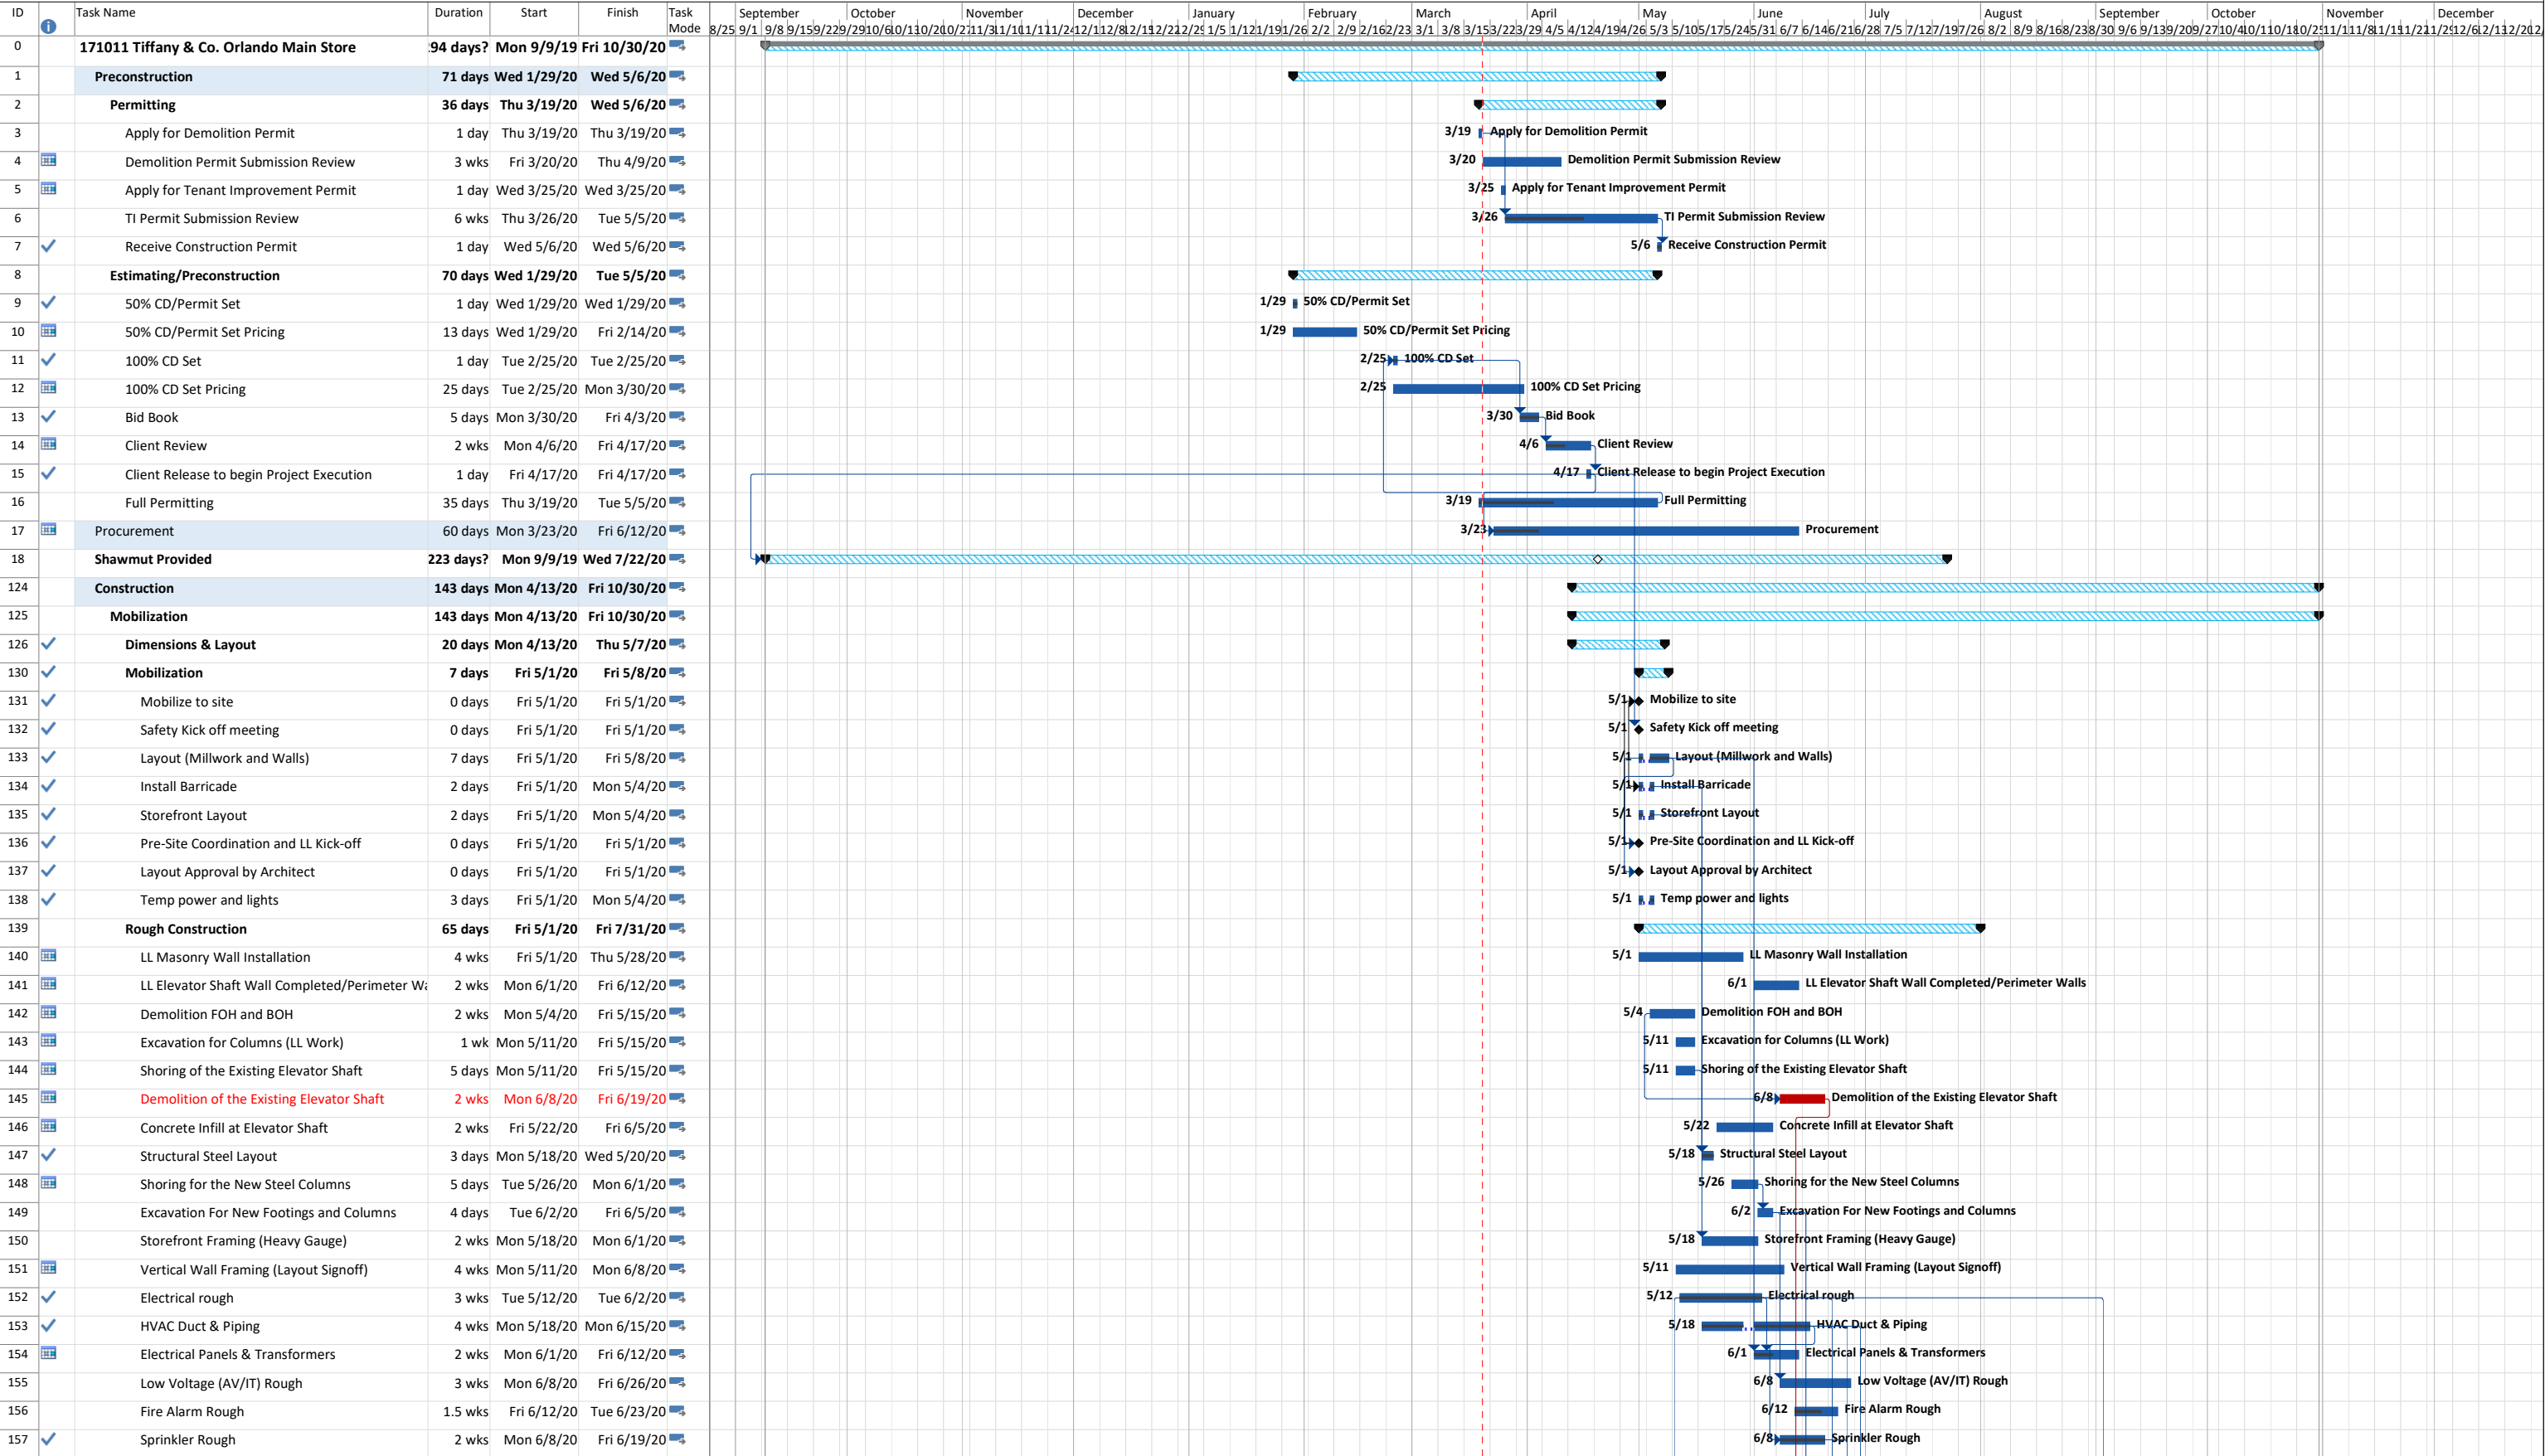

DRAFT

ID	Task Name	Duration	Start	Finish	Task Mode	September	October	November	December	January	February	March	April	May	June	July	August	September	October	November	December
158	Install & Flashing at Equipment Rails	5 days	Mon 6/22/20	Fri 6/26/20												6/22	6/26				
159	Install FCU HVAC Equipment	2 wks	Mon 6/15/20	Fri 6/26/20												6/15	6/26				
160	Floor Leveling	10 days	Mon 6/15/20	Fri 6/26/20												6/15	6/26				
161	Plumbing rough	2 wks	Mon 6/29/20	Mon 7/13/20												6/29	7/13				
162	Fire Protection Rough	1 wk	Mon 6/22/20	Fri 6/26/20												6/22	6/26				
163	Ceiling Framing	3 wks	Fri 6/26/20	Fri 7/17/20												6/26	7/17				
164	Light Fixtures Rough	2 wks	Wed 7/1/20	Wed 7/15/20												7/1	7/15				
165	Linear Slot Diffuser install	2 wks	Tue 7/14/20	Mon 7/27/20												7/14	7/27				
166	Lighting Control Panels	1 wk	Mon 7/27/20	Fri 7/31/20												7/27	7/31				
167	Inspections: Rough MEPs, Framing, FP, LV	2 days	Thu 7/30/20	Fri 7/31/20												7/30	7/31				
168	Finishes	61 days	Mon 8/3/20	Tue 10/27/20																	
169	Drywall	2 wks	Mon 8/3/20	Fri 8/14/20												8/3	8/14				
170	Ceiling Drywall	4 wks	Mon 8/10/20	Fri 9/4/20												8/10	9/4				
171	Stone Portals	2 wks	Mon 8/17/20	Fri 8/28/20												8/17	8/28				
172	Tile Flooring	2 wks	Mon 8/31/20	Mon 9/14/20												8/31	9/14				
173	Doors & Frames	2 wks	Tue 9/15/20	Mon 9/28/20												9/15	9/28				
174	Stone Walls	1.5 wks	Mon 10/5/20	Wed 10/14/20												10/5	10/14				
175	GFRG	2 wks	Mon 8/17/20	Fri 8/28/20												8/17	8/28				
176	Painting/Wall Covering	1 wk	Mon 8/31/20	Fri 9/4/20												8/31	9/4				
177	Millwork	34 days	Mon 9/7/20	Fri 10/23/20																	
178	Install Perimeter Millwork	3.5 wks	Mon 9/7/20	Thu 10/1/20												9/7	10/1				
179	Install VIP Millwork	2 wks	Fri 10/2/20	Thu 10/15/20												10/2	10/15				
180	Install Interior Glass and Mirror	2 wks	Mon 10/12/20	Fri 10/23/20												10/12	10/23				
181	Freestanding Millwork / Table Install / Vitrine	3 days	Thu 10/1/20	Tue 10/6/20												10/1	10/6				
182	Millwork Lighting	4 days	Mon 10/19/20	Thu 10/22/20												10/19	10/22				
183	Plumbing Finishes	2 days	Mon 8/31/20	Tue 9/1/20												8/31	9/1				
184	Electrical Finishes	4 days	Thu 9/3/20	Wed 9/9/20												9/3	9/9				
185	Interior Signage	1 day	Tue 9/8/20	Tue 9/8/20												9/8	9/8				
186	ACT Tile	5 days	Tue 9/8/20	Mon 9/14/20												9/8	9/14				
187	Carpet Install	3 days	Tue 9/8/20	Thu 9/10/20												9/8	9/10				
188	Fire Alarm Finishes	2 days	Tue 9/15/20	Wed 9/16/20												9/15	9/16				
189	Light Fixture Finishes	2 days	Tue 9/15/20	Wed 9/16/20												9/15	9/16				
190	Fire Protection finishes	2 days	Tue 9/15/20	Wed 9/16/20												9/15	9/16				
191	Lighting Control Commissioning	3 days	Thu 9/17/20	Mon 9/21/20												9/17	9/21				
192	Ceiling Painting	3 days	Mon 9/21/20	Wed 9/23/20												9/21	9/23				
193	Telephone / Data / AV	2 days	Mon 9/21/20	Tue 9/22/20												9/21	9/22				
194	Intrusion System	2 days	Mon 9/21/20	Tue 9/22/20												9/21	9/22				
195	Low Voltage Finishes	2 days	Mon 9/21/20	Tue 9/22/20												9/21	9/22				
196	Henderson Commisioning Site Visit	2 days	Fri 10/23/20	Mon 10/26/20												10/23	10/26				
197	Final Clean	2 days	Mon 10/26/20	Tue 10/27/20												10/26	10/27				
198	Close out	1 day	Fri 10/30/20	Fri 10/30/20												10/30	10/30				
199	Final Inspection/Walk Through/Closeout	3 days	Wed 10/28/20	Fri 10/30/20																	
200	Final Inspections (MEP's)	3 days	Wed 10/28/20	Fri 10/30/20																	
201	Create Punchlist	1 day	Wed 10/28/20	Wed 10/28/20												10/28	10/28				
202	FD Life Safety Inspection	2 days	Wed 10/28/20	Thu 10/29/20												10/28	10/29				
203	Building Inspection	1 day	Thu 10/29/20	Thu 10/29/20												10/29	10/29				
204	Final Clean	1 day	Fri 10/30/20	Fri 10/30/20												10/30	10/30				
205	Substantial Completion	1 day	Fri 10/30/20	Fri 10/30/20												10/30	10/30				
206	Turn over to Client	0 days	Fri 10/30/20	Fri 10/30/20												10/30	10/30				
