


ID		Task Mode	Task Name	Duration	Start	Finish	22	T	W	T	F	S	Oct 30, '22	S	M	T	W	T	F	S	Nov 6, '22	S	M	T	W
1			Install Barricade Wall	3 days	Mon 11/21/22	Wed 11/23/22																			
2			Demo	4 days	Thu 11/24/22	Tue 11/29/22																			
3			Framing	5 days	Wed 11/30/22	Tue 12/6/22																			
4			MEP's rough-in	5 days	Wed 12/7/22	Tue 12/13/22																			
5			Inspections	1 day	Wed 12/14/22	Wed 12/14/22																			
6			Hang and finish drywall	7 days	Thu 12/15/22	Fri 12/23/22																			
7			X-Mas/Holiday Break	7 days	Sat 12/24/22	Sun 1/1/23																			
8			Floor prep	1 day	Mon 1/2/23	Mon 1/2/23																			
9			Wood floor install	3 days	Tue 1/3/23	Thu 1/5/23																			
10			Wood trim/Door install	5 days	Fri 1/6/23	Thu 1/12/23																			
11			Prep/Paint	3 days	Fri 1/13/23	Tue 1/17/23																			
12			Wall coverings	3 days	Wed 1/18/23	Fri 1/20/23																			
13			MEP's trim	4 days	Mon 1/23/23	Thu 1/26/23																			
14			Barricade removal/drywall,paint touch up/ window film removal	1 day	Fri 1/27/23	Fri 1/27/23																			
15			Install carpet	2 days	Mon 1/30/23	Tue 1/31/23																			
16			Fixture install	2 days	Wed 2/1/23	Thu 2/2/23																			
17			Final inspections	2 days	Fri 2/3/23	Mon 2/6/23																			
18			Walk and punch	2 days	Tue 2/7/23	Wed 2/8/23																			

--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--

Project: Saks, VIP Room (Palm B) Date: Wed 10/26/22	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

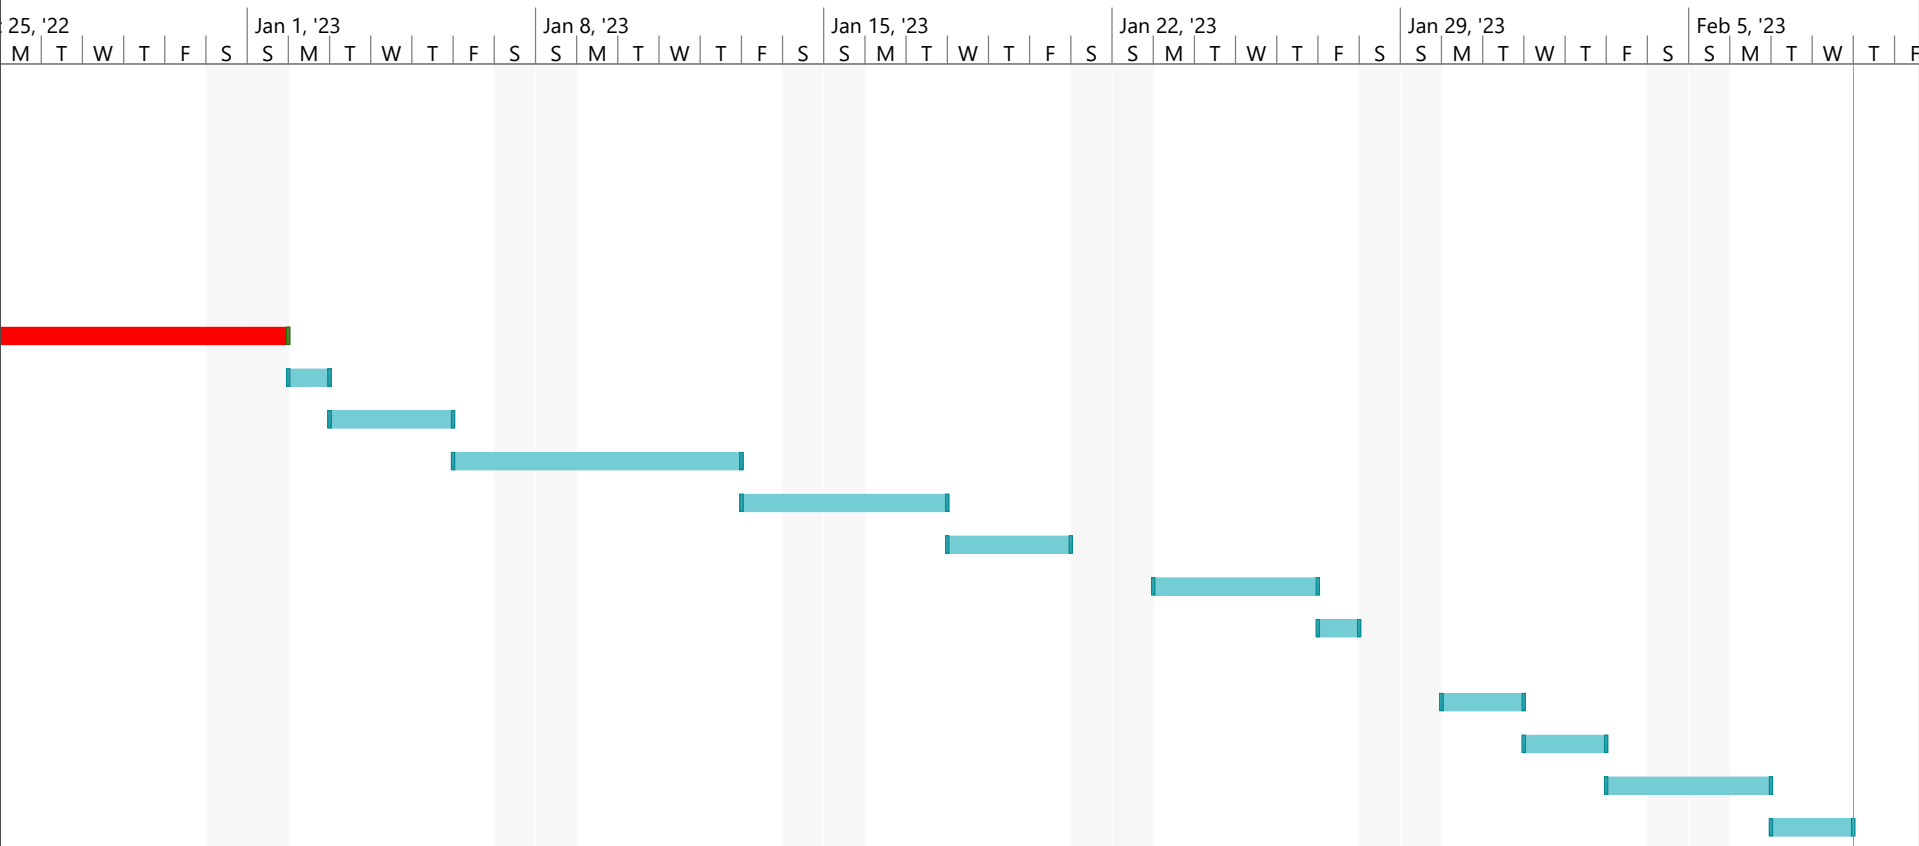

Project: Saks, VIP Room (Palm B) Date: Wed 10/26/22	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			
