The Palm Beach Orthodox Synagogue
Expansion and Renovation Project
120-132 N COUNTY ROAD

PALM BEACH SYNAGOGUE

Bartholemew + Partners
ARCHITECTURE AND DESIGN
PROGETTO DI ARCHITETTURA

ID	Task Mode	Task Name	Duration	Start	Finish
1		Mobilize/Secure Site	15 days	Mon 5/5/25	Fri 5/23/25
2		Complete Demo	40 days	Mon 5/26/25	Fri 7/18/25
3		Auger Cast/Concrete Shell	200 days	Mon 7/21/25	Fri 4/24/26
4		Utilities and Site Work	100 days	Mon 9/15/25	Fri 1/30/26
5		Dry-In Envelope	60 days	Mon 3/2/26	Fri 5/22/26
6		Façade Finishes /Stone Cladding/Stucco/Exterior Painting	100 days	Mon 5/25/26	Fri 10/9/26
7		Hardscape/Planting/Railings	40 days	Mon 10/12/26	Fri 12/4/26
8		Interior Framing	50 days	Mon 3/2/26	Fri 5/8/26
9		M/E/P Rough-Ins	65 days	Mon 4/13/26	Fri 7/10/26
10		Drywall	60 days	Mon 7/13/26	Fri 10/2/26
11		Millwork/Finishes	80 days	Mon 10/5/26	Fri 1/22/27
12		Trim Out/FFE	50 days	Mon 1/25/27	Fri 4/2/27
13		Final Inspections	20 days	Mon 4/5/27	Fri 4/30/27

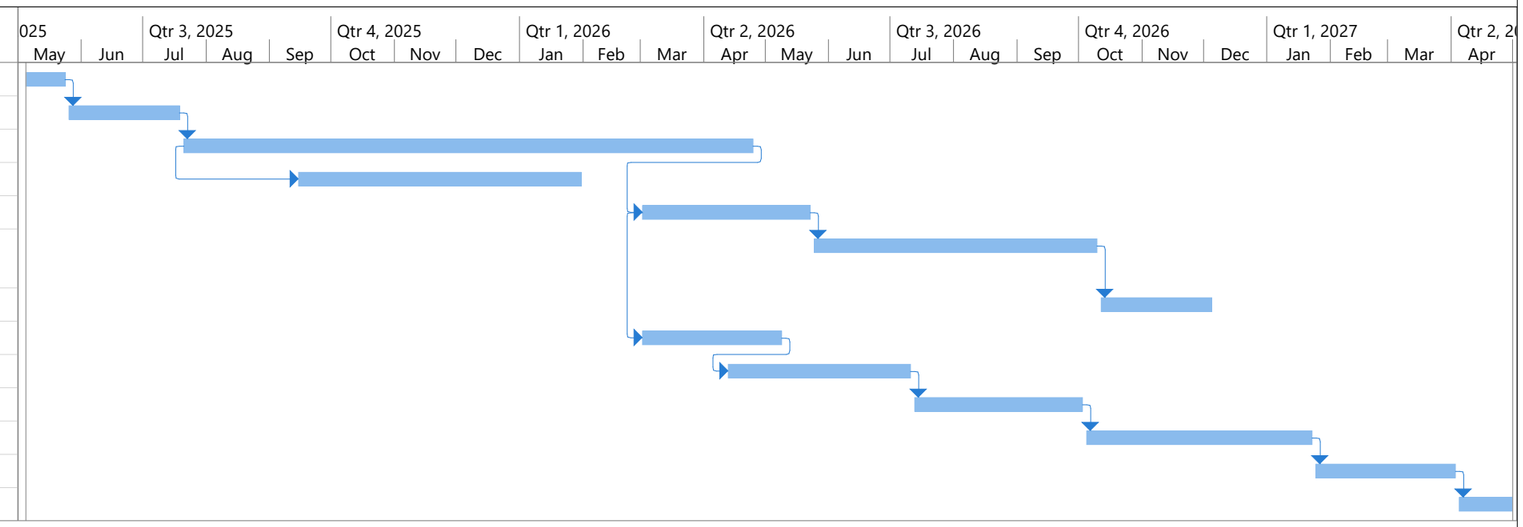

CONKLING & LEWIS CONSTRUCTION, INC.
GENERAL CONTRACTORS
CONSTRUCTION MANAGERS

Conceptual Schedule
10/11/2024

ZABIK AND ASSOCIATES, INC.
